
#	Name	0	Planned Duration	Start Date	Completion Date	%	Pre dec f
1	IRTP C Rec. 3 Implementation	•	1 days	5/1/14 8:00 AM	5/2/14 8:00	0.0	
2	Announce Implementation to Registrars/Registries	•	1 days	5/1/14 8:00 AM		0.0	
3	IRTP C Rec. 2 Implementation		<u> </u>	3/7/14 6:00 AM	8/18/14 8:00	0.0	
4	Develop work plan and implementation timeline	1	10 days	3/7/14 6:00 AM	3/20/14 2:00	+	
5	Provide work plan to IRT for feedback	•	5 days	4/14/14 8:00 AM	4/21/14 8:00	+	4
6	Finalize implementation timeline (ICANN Staff)		2 days	4/21/14 8:00 AM	4/23/14 8:00	+	5
7	Draft FOA policy language (ICANN Staff)		10 days	4/23/14 8:00 AM	5/7/14 8:00	0.0	6
8	Present proposed policy language to IRT for feedback (ICANN Staff + IRT)		10 days	5/7/14 8:00 AM	5/21/14 8:00	0.0	7
9	Update policy language and present to IRT (ICANN Staff)		7 days	5/21/14 8:00 AM	6/2/14 8:00	0.0	8
10	Hold call w IRT for final feedback before public comment period		5 days	6/2/14 8:00 AM	6/9/14 8:00	0.0	9
11	Post proposed policy language for public comment		45 days	6/9/14 8:00 AM	8/12/14 8:00	0.0	10
12	Summarize public comments and finalize language		10 days	8/4/14 8:00 AM	8/18/14 8:00	0.0	11
13	IRTP C Rec. 1 Implementation		271 days	6/1/14 12:00 AM	5/1/15 2:00	0.0	
14	Create draft inter-registrant policy framework:		20.38 days	6/1/14 12:00 AM	6/30/14 8:00	0.0	
15	Define list of circumstances in which inter-registrant transfers should be permitted/prohibited (Staff and		10 days	6/1/14 12:00 AM	6/13/14 2:00	0.0	
16	Finalize terms for availability of inter-registrant transfers with IRT.	•	5 days	6/15/14 12:00 AM	6/20/14 2:00	0.0	
17	(Face to face) IRT white-boarding session in London to define (draft) model of inter-registrant transfer	•	3.38 days	6/25/14 5:00 AM	6/30/14 8:00	0.0	
18	Define the process through which the losing registrant authorizes the transfer. (Staff + IRT)	•	1 days	6/25/14 5:00 AM	6/25/14 2:00	0.0	
19	Define the process through which the receiving registrant authorizes the transfer. (Staff + IRT)	•	1 days	6/26/14 8:00 AM	6/27/14 8:00	0.0	
20	Identify differences between registrar validation of transfers in thick and thin registries and added		1 days	6/26/14 8:00 AM	6/27/14 8:00	0.0	
21	Define the rules for registrar locks on domains following an inter-registrant transfer, including		1 days	6/27/14 8:00 AM	6/30/14 8:00	0.0	
22	Draft skeletal outline of change of registrant portion of Transfer Policy. (Staff + IRT)		1 days	6/26/14 8:00 AM	6/27/14 8:00	0.0	
23	Draft inter-registrant policy language following input from IRT in London (ICANN Staff)	•	20 days	6/27/14 8:00 AM	7/28/14 8:00	0.0	22
24	Calls w IRT to continue defining inter-registrant transfer process, as needed (ICANN Staff + IRT)	•	20 days	6/27/14 8:00 AM	7/28/14 8:00	0.0	
25	Share proposed domain transfer policy for input with IRT		10 days	7/28/14 8:00 AM	8/11/14 8:00	0.0	24
26	Meeting(s) to discuss/review policy language		1 days	8/11/14 8:00 AM	8/12/14 8:00	0.0	25
27	Post for public comment, as final domain transfer policy, including other recommendations		45 days	8/12/14 8:00 AM	10/15/14	0.0	26,
28	Summarize public comments and finalize language		11 days	10/15/14 8:00 AM	10/30/14	0.0	27
29	Announce implementation to registries and registrars	•	1 days	10/31/14 5:00 AM	10/31/14	0.0	28
30	Policy Effective Date		1 days	5/1/15 5:00 AM	5/1/15 2:00	0.0	29
31	IRTP C Rec. 1 and Rec. 2 Outreach and Education		25 days	11/3/14 6:00 AM	12/9/14 3:00	0.0	
32	Update registrar training program to reflect new registrar requirements		10 days	11/3/14 6:00 AM	11/14/14	0.0	29
33	Conduct community outreach and industry education		15 days	11/17/14 6:00 AM	12/9/14 3:00	0.0	
34	Update ICANN website and IRTP FAQ pages		10 days	11/17/14 6:00 AM	12/2/14 3:00	0.0	32
		1		10/2/14 6 00 111			1

5 days

12/3/14 6:00 AM

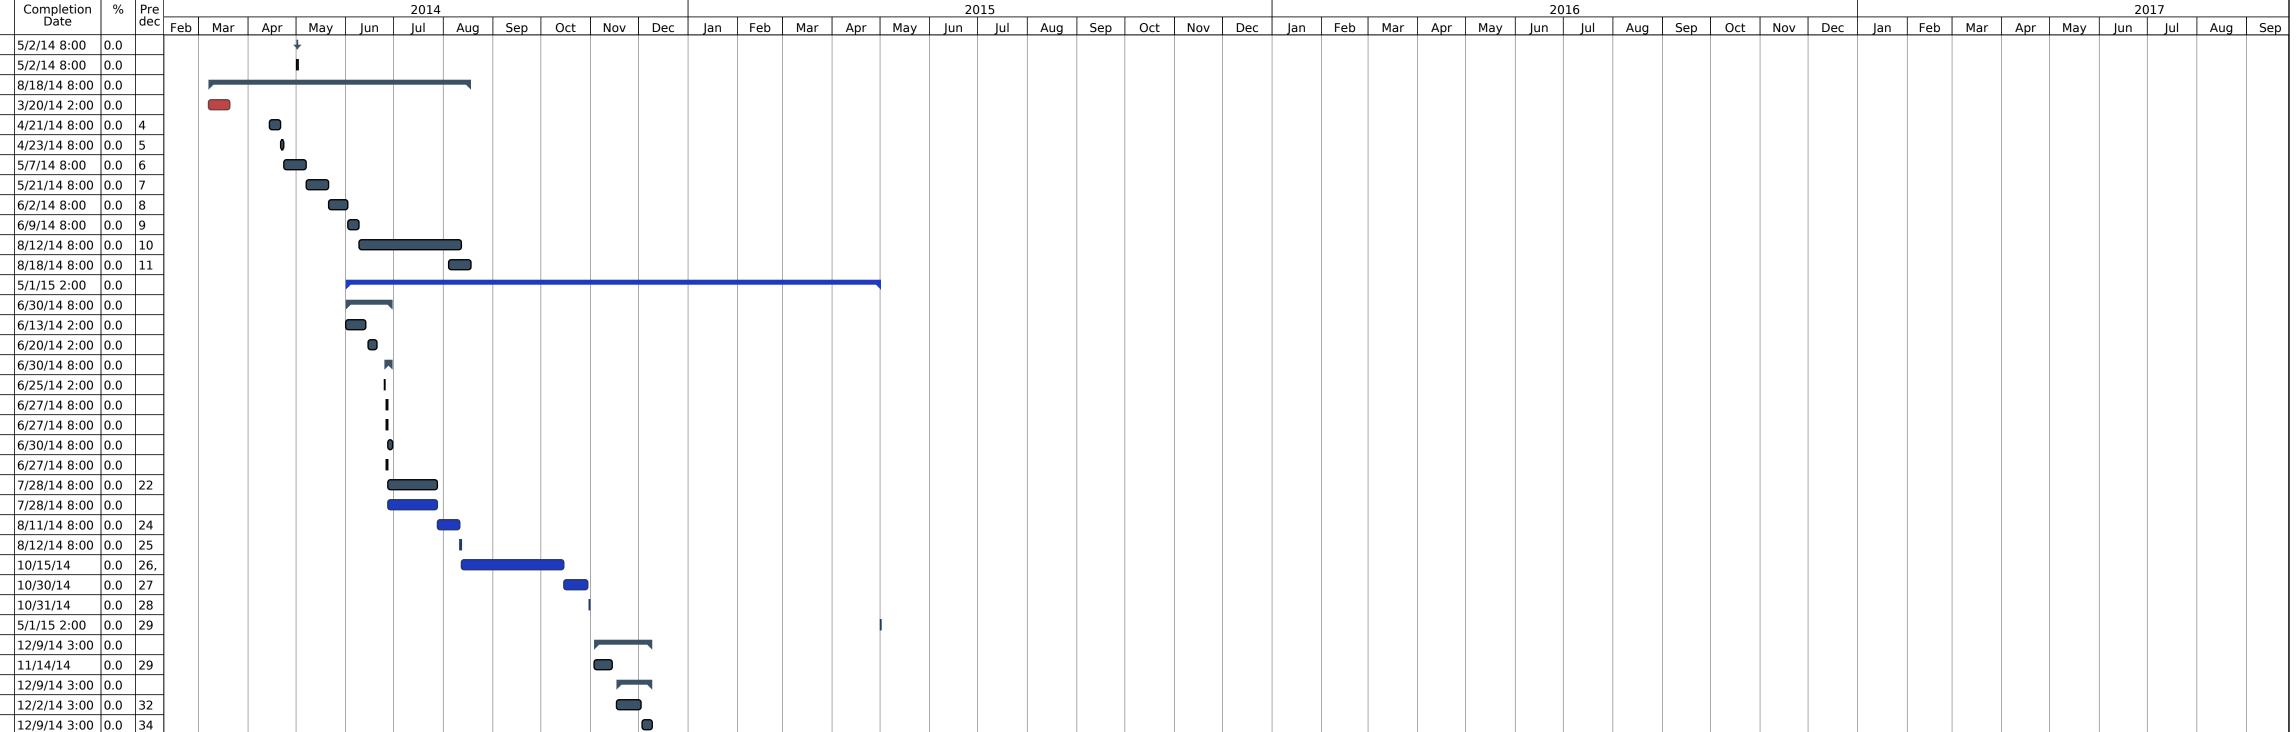

Conduct a webinar for registrars and registries
